PRESENTATION Villa Larsson

3D PlanAssembly

VILLA LARSSON

▷ ASSEMBLING PLAN ◁

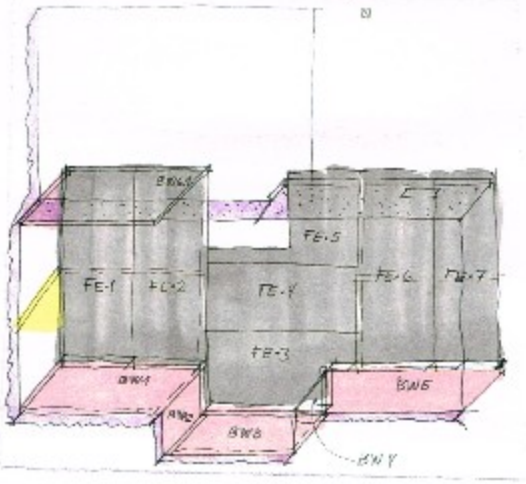

(Load into FE materials for use in 2nd Floor)
(80 MIN)

FLOORING ELEM.
FE·1 → FE·7

TIRD. ASSEMBLE
(120 MIN)
(Load into basement materials
(60 MIN.)

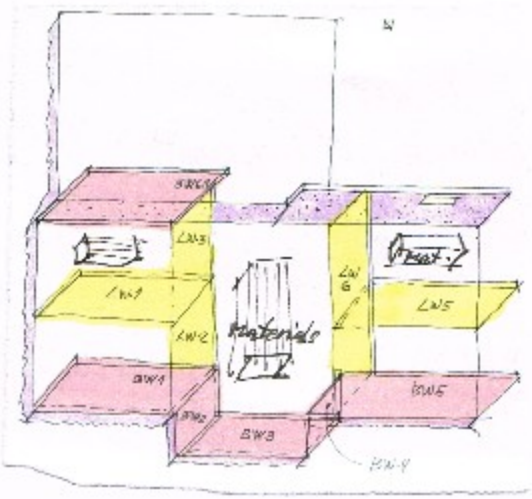

LOADING WALLS
LW-1 → LW-6

SECOND ASSEMBLE
(75 MIN.)

BASEMENT WALLS
BW 6.1 - BW1 → BW5

START: First assemble
(75 MIN.)

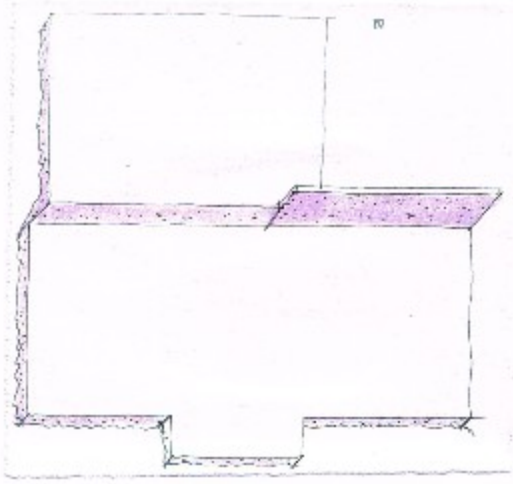

FUNDAMENT ON
2 PLANS (insulated)

▷ ASSEMBLING PLAN ◁

VILLA LARSSON

MEASURED ASSEMBLE TIME 1.055 MIN. 18 HOUR

(Load Rukki on the Roof)
(30 MIN)

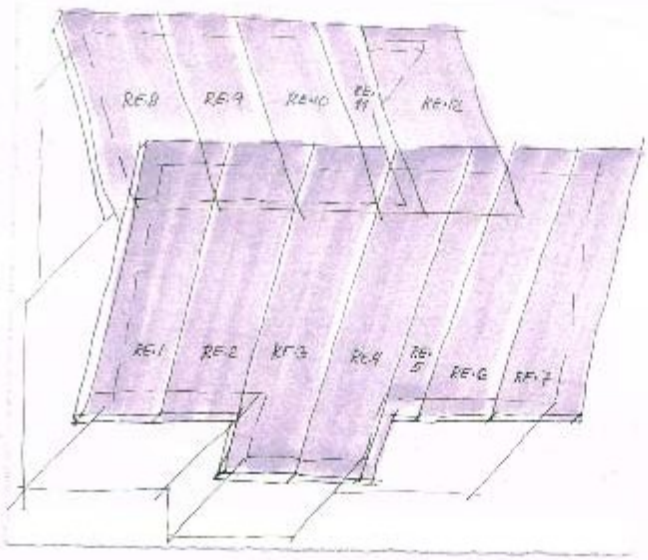

ROOFING ELEM.

RE1 → RE 12

FIFTH ASSEMBLE
(240 MIN.)

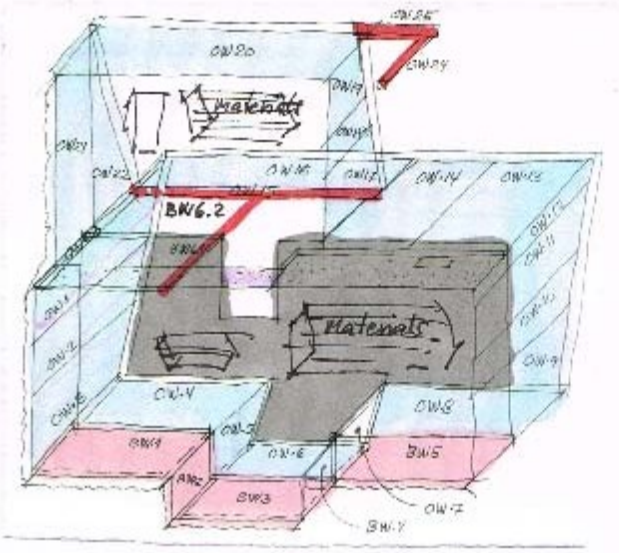

(Load into 1. floor materials for use there)
(75 MIN.)

OUTSIDE WALL ELEMENT

OW-1 → OW 23

Fourth ASSEMBLE
(360 MIN.)

Architectural Drawings - Plan

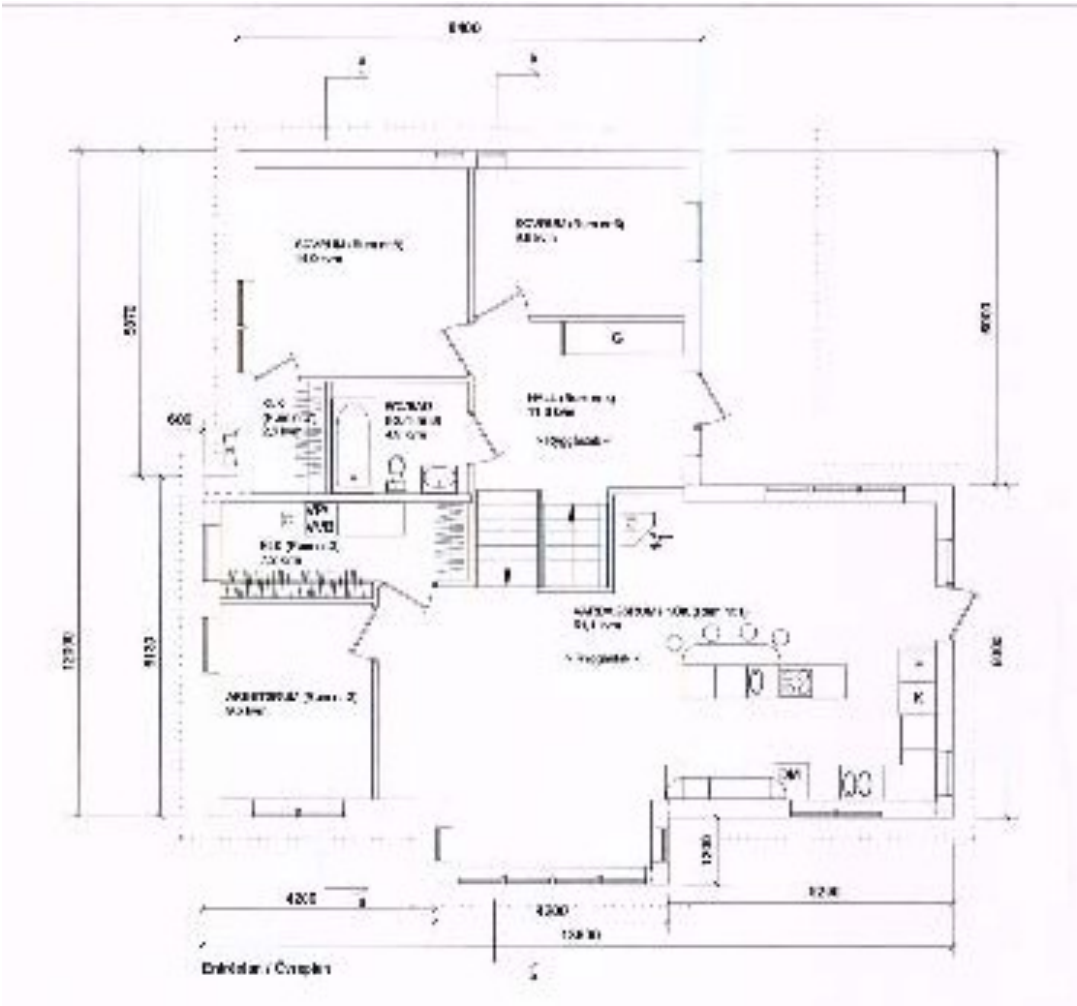

Lower and Upper Ground Floor Plan

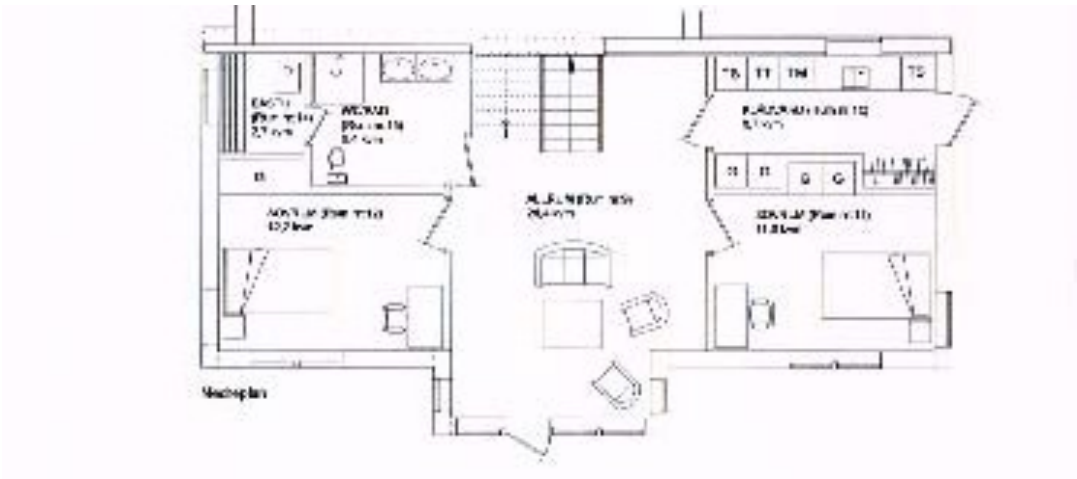

Basement Plan

Architectural Drawings - Section

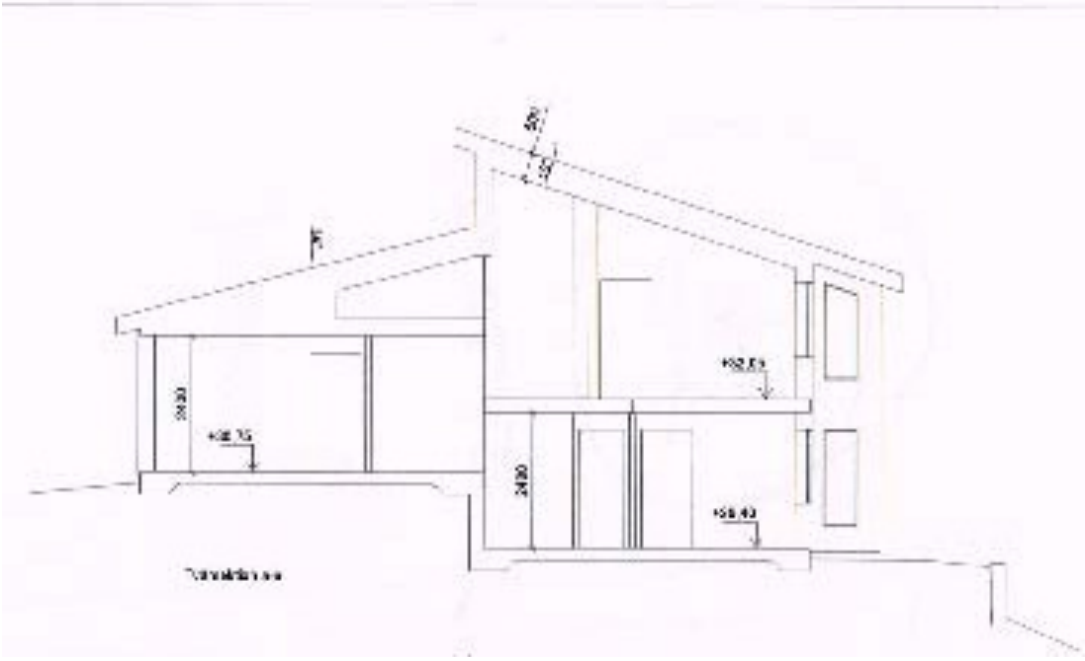

Section

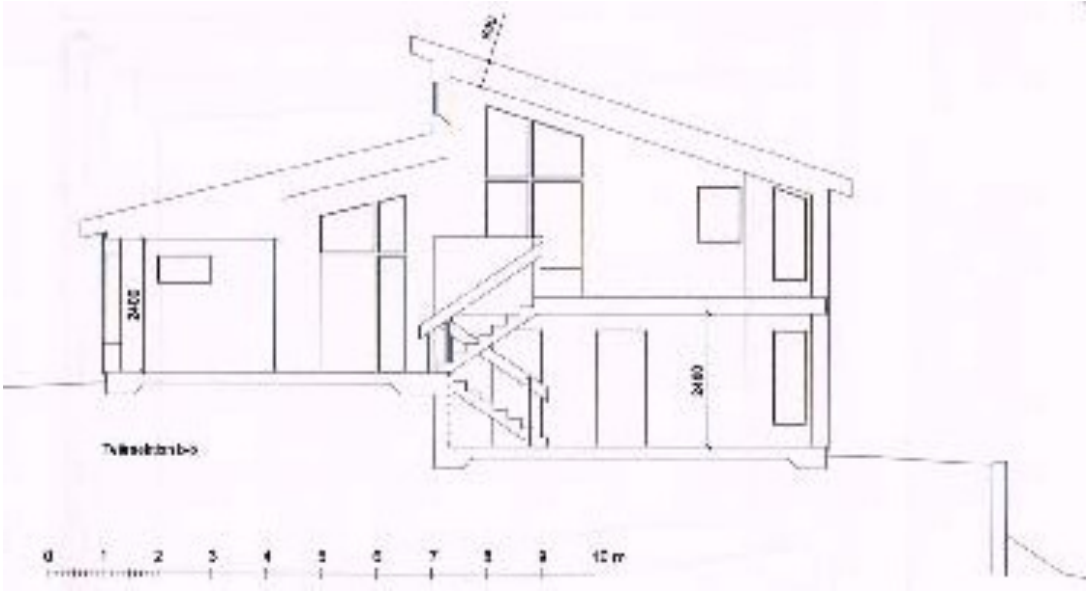

Section

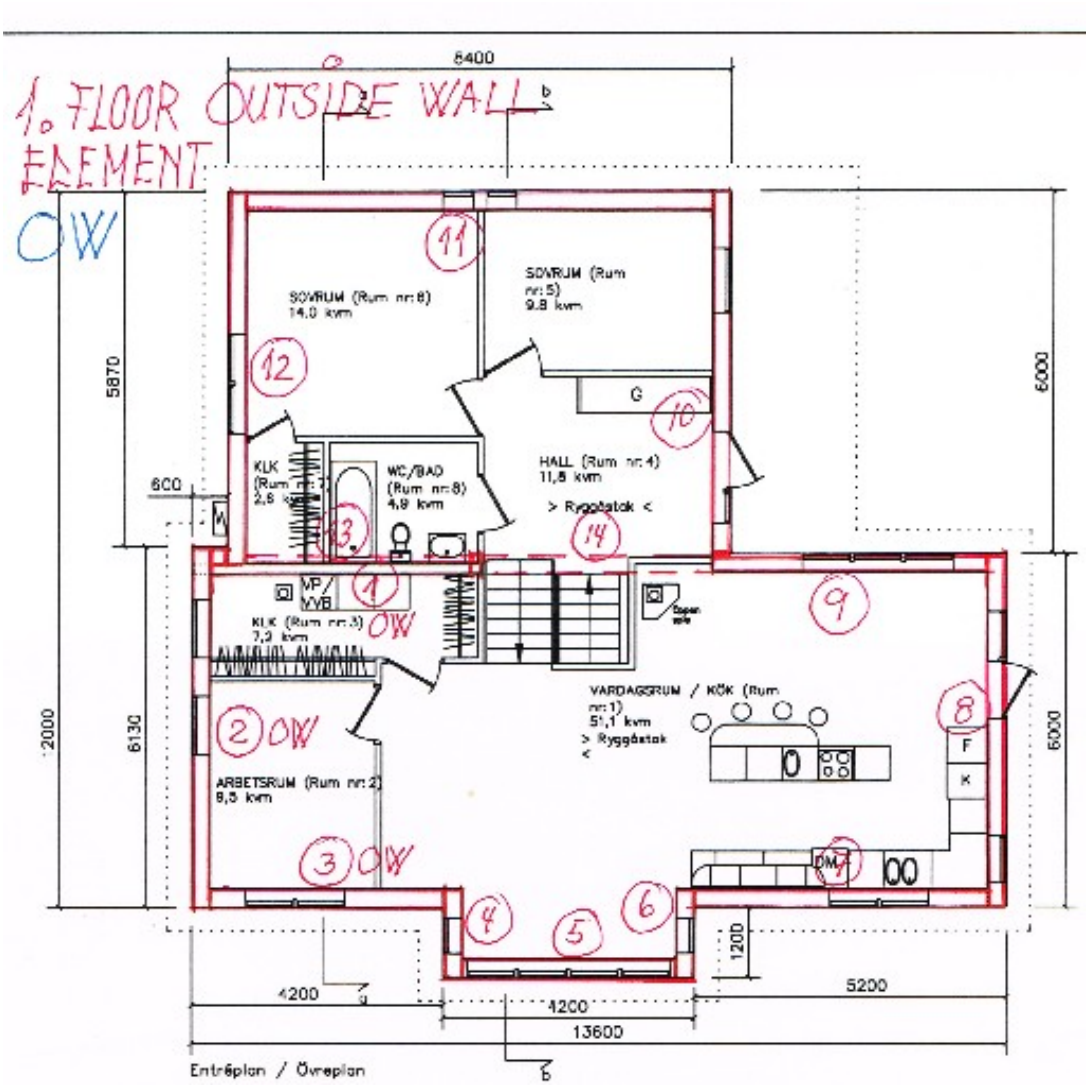

Element Plan - Ground Floor

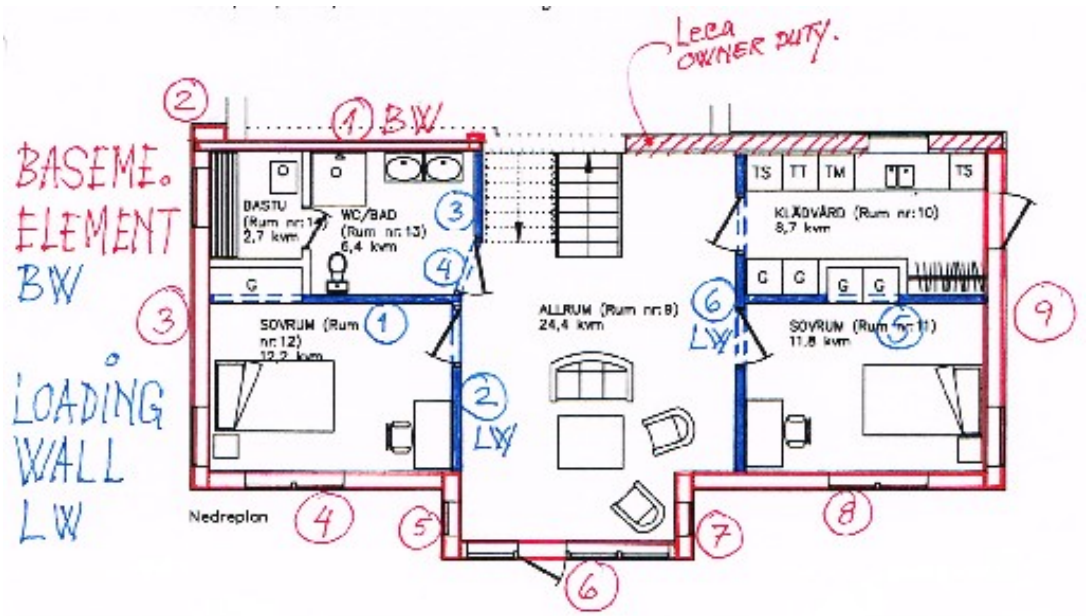

Element Plan - Basement Floor

Architectural Drawings - Element Plan

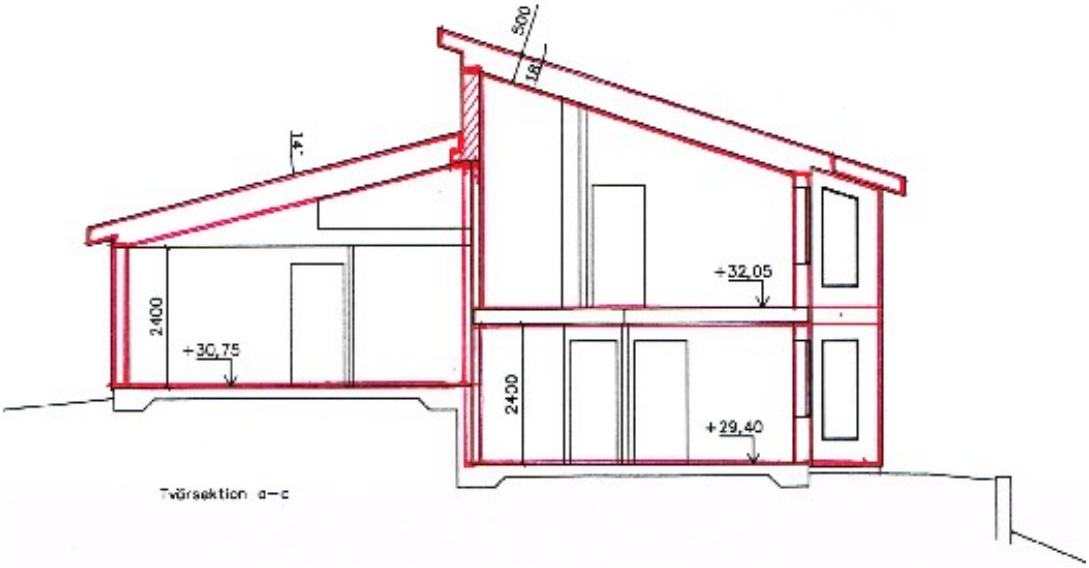

Section

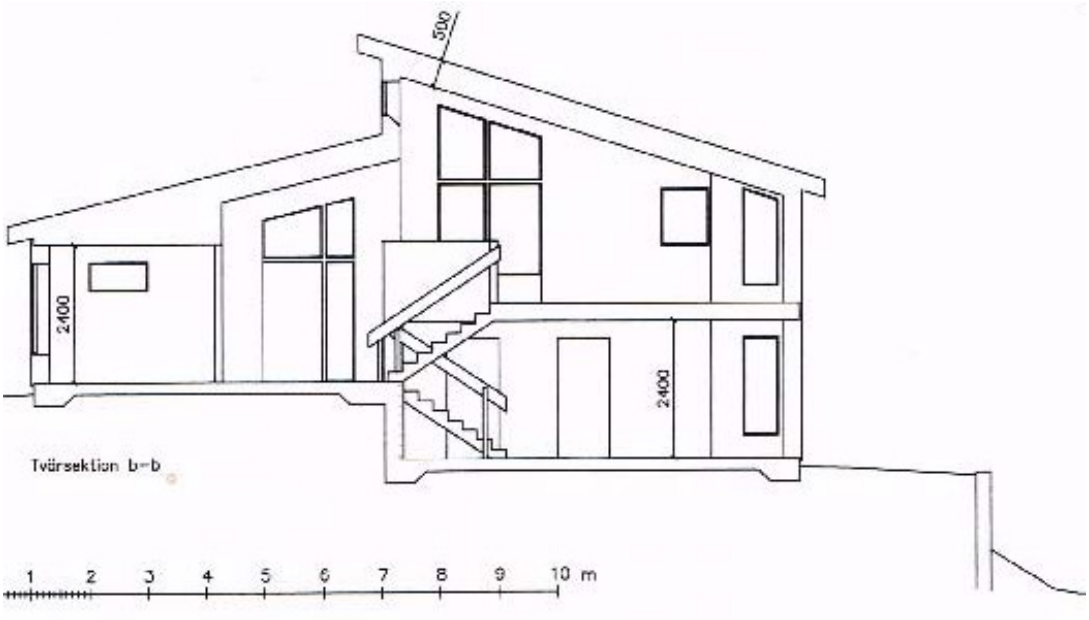

Section

Construction site - Montage

1. Concrete plate at site is ready for element assembly/installation.

2. Concrete/masonry walls at basement are ready for element assembly/ installation.

3. Concrete plate at site is ready for element assembly/installation.

4. Wall Elements installed at basement floor.

5. Wall Elements installed at basement floor.

6. Floor Elements installed at basement floor.

7. Crane lifting elements and positioning for placement.

8. Floor Elements are position installation.

9. Wall elements are installed.

10. Element installation.

11. Element installation.

12. Element installation.

13. Element installation.

14. Element installation.

15. Element installation.

16. Element installation.

17. Element installation.

18. Element installation.

19. Element installation.

20. Element installation.

21. Element installation.

22. Element installation finished.

23. Element installation. Finished and finishing works started.

24. Element installation. Finished and finishing works started.

25. Element installation. Finished and finishing works started.

26. Installation finishing materials.

27. Electrical installation.

28. Electrical installation.

29. ElecElectrical /Plumbing installation.

30. Finishing works in progress.

31. Painting works and floor installation.

Construction site - Completed

01. House finished.

02. View at porch.

03. View from corner.

04. View at porch.

Finished Building - Exterior

01. View from road.

02. View from farther road.

Finished Building - Exterior

03.

04.

Finished Building - Exterior

05.

06.

07.

08. Porch view at night.

Finished Building - Interior

01.

02.

03.

04.

05.

06.

07.

08.

09.

10.

11.

12.

13.

14.

15.

16.

17.

18.

AA-BOX Sp Z o.o

E-mail: info@plusshus.no
